BRUHAT BENGALURU MAHANAGARA PALIKE

Clients Name	:	Executive Engineer Yelahanka Division
Project Name	:	Construction of additional class rooms and compound wall at Govt. Higher primary school (Bangala school) at Yelahanka Old Town in Kempegowda ward no: 01.
Consultants	:	Rudraprasad Consultants
Project Manager /Team Leader	:	Karthik Rechan
Project Start Date	:	20-01-21
Project End Date	:	08-02-23
Project Length in Months	:	25 Months

Sl. No	Assignment	Unit	Modified Schedule Qty	Qty of Work done	% Of Work done	Start Date	End Date	No. of Working Days
1	Dismantling of existing structures like culverts, bridges, retaining walls and other structure comprising of masonry, cement concrete, wood work, steel work, including T&P and scaffolding wherever necessary, sorting the dismantled material, disposal of unserviceable material and stacking the serviceable material with	Sqm	55.4	55.4	100	25-01-21	14-02-21	20
2	Dismantling of existing structures like culverts,bridges, retaining walls and other structure comprising of masonry, cement concrete, wood work, steel work, including T&P and scaffolding wherevernecessary, sorting the dismantled material, disposal of unserviceablematerial and stacking the serviceable material with	Cum	129.2	129.2	100	30-01-21	09-02-21	10
3	Dismantling cement concrete flooring or plain cement concrete work including removing and conveying the debris to distance upto 200m (within average thickness of 15 cms)Complete as per specifications and the directions of the Engineer-in-charge	Cum	214.24	214.24	100	09-02-21	01-03-21	20
4	Dismantling plastering and removing the debris with a lead upto 200m.Complete as per specifications and the directions of the Engineer-in-charge	Cum	616.57	616.57	100	17-02-21	14-03-21	25
5	Earth work for lowering and levelling the ground other than foundation works by mechanical means upto 3.00 depth, including providing shoring and strutting, removal of stumps and other deleterious matter, dressing of sides and bottom, filling back the excavation earth to the extent required including the cost of labour	tonne	59.13	59.13	100	27-02-21	18-04-21	50
6	Conveying the excavated earth, debries etc., with all lead and lifts including loading and unloading charges etc., complete as per the direction of the Engineer-in-charge.	Cum	288.2	288.2	100	04-03-21	29-03-21	25
7	Removing and Reinstalation of RO Plant(Data rate)	Sqm	1	0	0	20-01-21	08-02-23	749
8	Earthwork excavation for foundation of buildings, water supply, sanitary lines and electrical conduits either in pits or in trenches 1.5m and above in width, in hard soil not exceeding 1.5 m. in depth including dressing the bottom and sides of pits and trenches, stacking the exavated soil clear from edges of excavation with	Sqm	615.91	1097.33	100	08-04-21	03-05-21	25
9	Providing and Filling in foundation with granite / trap broken metal 100mm. and down size, with approved sand including hand packing, ramming, watering, including cost of all materials and labour with all lead and lift. Complete as per specifications and the directions of the Engineer-in-charge	Sqm	69.28	68.31	99	13-05-21	23-05-21	10
10	Providing and laying in position plain cement concrete of mix 1:4:8(M7.5)with OPC cement @ 180kgs, with 40mm and down size graded granite metal coarse aggregates @0.85cum and fine aggregtes @ 0.57cum machine mixed, machine mixed, concrete laid in layers not exceeding 15 cms. thick, well compacted, in foundation including cost of all materials, labour, HOM of machinery, curing Complete as per specifications and the	Cum	65.91	78.71	100	31-05-21	15-06-21	15
11	Providing and laying in position plain cement concrete of mix M15 with cement @ 240kgs, with 20mm and down size graded granite metal coarse aggregates @0.878cum and fine aggregtes @ 0.53cum, machine mixed, concrete laid in layers not exceeding 15 cms. thick, well compacted, in foundation,plinth and cills,	M	108.96	107.42	99	22-06-21	07-07-21	15
12	Providing and constructing granite / trap / basalt size stone masonry in foundation cement mortar 1:6, stone hammerddressed in courses not less than 20 cms high, bond stones at 2m apart in each course including cost of materials, labour, curing Complete as per specifications and the directions of the Engineer-in-charge	Sqm	92.97	91.21	98	15-07-21	23-07-21	10
13	Filling available excavated earth (excluding rock) in sides of foundations upto plinth in layers not exceeding 20 cms. in depth, compacting each deposited layer by ramming after watering with lead upto 50 m. and lift upto 1.5 m. including cost of all labour Complete as per specifications and the directions of the Engineer-	Cum	118.51	615.62	100	25-07-21	09-08-21	15

Asst. Executive Engineer
Yelahanka Sub Divison
(BBMP Ynk. Zn)
Yelahanka, Bangalore

CamScanner

BRUHAT BENGALURU MAHANAGARA PALIKE

Clients Name	:	Executive Engineer Yelahanka Division
Project Name	:	Construction of additional class rooms and compound wall at Govt. Higher primary school (Bangala school) at Yelahanka Old Town in Kempegowda ward no: 01.
Consultants	:	Rudraprasad Consultants
Project Manager /Team Leader	:	Karthik Rechan
Project Start Date	:	20-01-21
Project End Date	:	08-02-23
Project Length in Months	:	25 Months

Sl. No	Assignment	Unit	Modified Schedule Qty	Qty of Work done	% Of Work done	Start Date	End Date	No. of Working Days
14	Conveying the excavated earth, debries etc., with all lead and lifts including loading and unloading charges etc., complete as per the direction of the Engineer-in-charge.Complete as per specifications and the directions of the Engineer-in-charge	Each	497.4	481.71	97	08-04-21	03-05-21	25
15	Providing and removing centering, shuttering, strutting, propping etc., and removal of form work for foundations, footings, bases of columns for mass concrete including cost of all materials, labour Complete as per specifications and the directions of the Engineer-in-charge Qty upto 125%	Each	315.19	446.05	100	14-08-21	23-09-21	40
16	Providing and removing centering, shuttering, strutting, propping etc., and removal of form work for vertical surface such as walls at any thickness , including attached pilasters, buttresses, plinth and string courses cost of all materials, labour Complete as per specifications and the directions of the Engineer-in-charge	Cum	309.89	292.46	94	03-09-21	21-09-21	18
17	Providing and removing centering, shuttering, strutting, propping etc. and Removal of form Work for columns, pillars, piers, post and struts, square / rectangular / polygon in plan including cost of all materials, labour Complete as per specifications and the directions of the Engineer-in-charge	Cum	324.89	136.65	42	13-09-21	03-10-21	20
18	Providing and removing centering, shuttering, strutting, propping etc., and removal of form work for suspended floors, landings, balconies and likes, thickness upto 200 mm including cost of all materials, labour complete as per specificaitons for heights more than 3.50m from ground level. - 0 to 5 mtrs.Complete as per	Cum	1140.61	549.24	48	23-09-21	14-10-21	21
19	Providing and removing centering, shuttering, strutting, propping etc., for edges of slabs and breaks in floors including cost of all materials,labourComplete as per specifications and the directions of the Engineer-in-charge	Sqm	50.91	20.62	41	05-10-21	04-11-21	30
20	Providing and removing centering, shuttering, strutting, propping etc., and removal of form work for sides and soffits of beams, beam haunchings, cantilever girders, bressumers and lintels not exceeding 1m in depth including cost of all materials, labour Complete as per specifications and the directions of the Engineer-	Sqm	520.64	285.36	55	15-10-21	14-11-21	30
21	Providing and removing centering, shuttering, strutting, propping etc., and removal of form work for Stairs (excluding landing) except spiral staircase including cost of all materials, labour Complete as per specifications and the directions of the Engineer-in-charge	Cum	65.36	39.34	60	25-10-21	24-11-21	30
22	Providing and removing centering, shuttering, strutting, propping etc., for chajjas, corbels etc., including edges including cost of all materials, labourComplete as per specifications and the directions of the Engineer-in-charge	Sqm	48.3	44.03	91	09-11-21	14-12-21	35
23	Providing and laying in position reinforced cement concrete of Design mix M25 with OPC cement @ 340kgs, with 20mm and down size graded granite metal coarse aggregates @0.70 cum and fine aggregtes @ 0.47cum, with super plasticisers @ 3 liters confirming to is 9103-1999 reaffirmed-2008 at machine mixed,	Cum	252.54	314.47	100	18-09-21	17-11-21	60
24	Providing and laying in position reinforced cementconcrete of design mix M25 with OPC cement @ 340kgs, with 20mm and down size graded granite metal coarse aggregates @0.70cum andfine aggregtes @ 0.47cum,with superplastisiser @3lts confirming to IS 9103-1999 Reaffirmed-2008, machine mixed,	Sqm	25.77	28	100	20-10-21	13-01-22	85
25	Providing and laying in position reinforced cementconcrete of design mix M25 with OPC cement @ 340kgs, with 20mm and down size graded granite metal coarse aggregates @0.70cum andfine aggregtes @ 0.47cum,with superplastisiser @3lts confirming to IS 9103-1999 Reaffirmed-2008, machine mixed,	Sqm	24.85	0.00	0	20-10-21	09-11-21	20

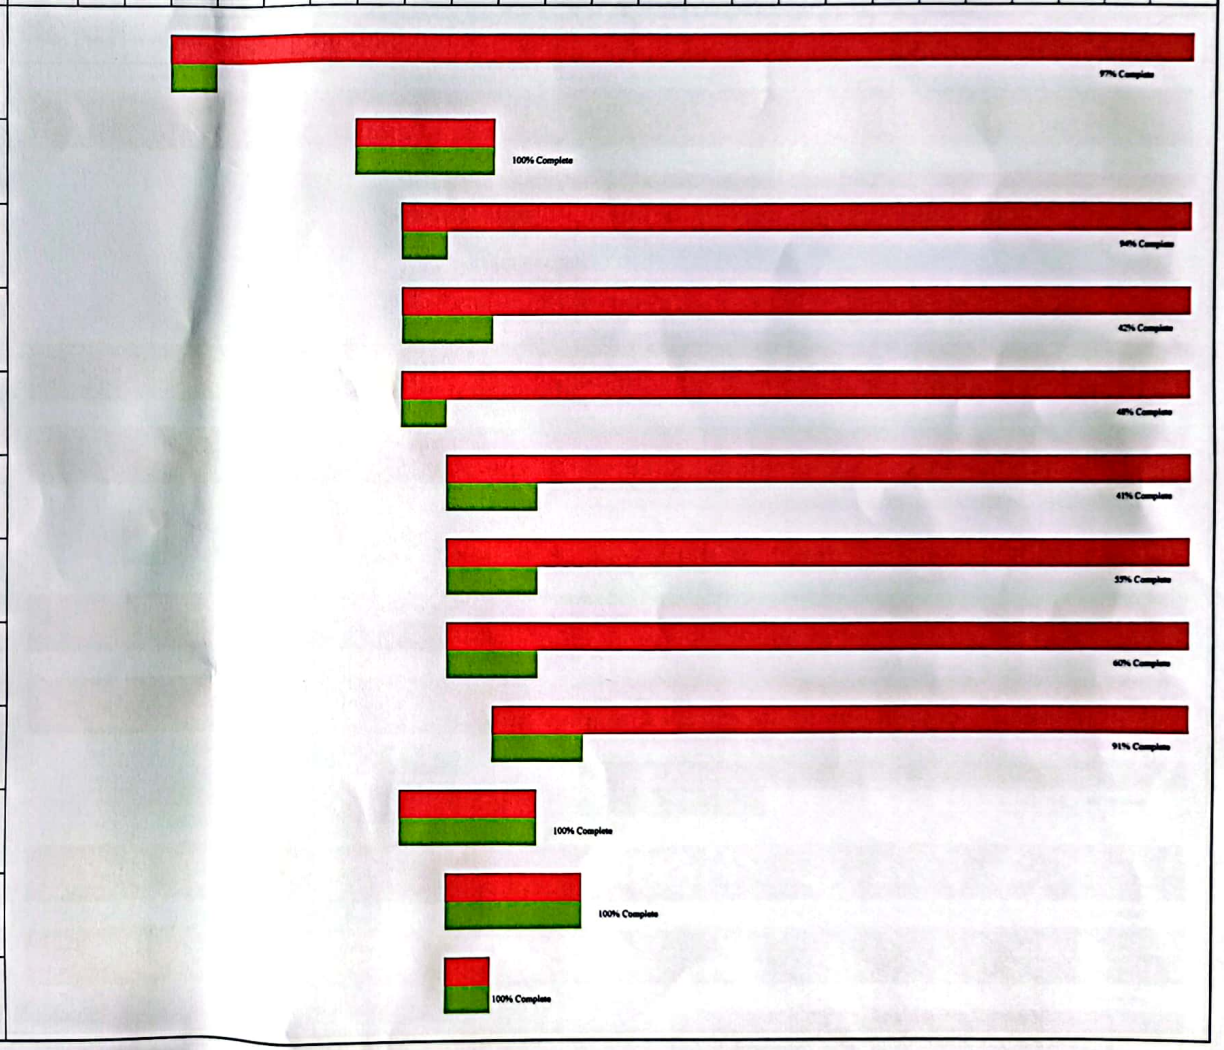

CamScanner

BRUHAT BENGALURU MAHANAGARA PALIKE

Clients Name	:	Executive Engineer Yelahanka Division
Project Name	:	Construction of additional class rooms and compound wall at Govt. Higher primary school (Bangala school) at Yelahanka Old Town in Kempegowda ward no: 01.
Consultants	:	Rudraprasad Consultants
Project Manager /Team Leader	:	Karthik Rechan
Project Start Date	:	20-01-21
Project End Date	:	08-02-23
Project Length in Months	:	25 Months

Sl. No	Assignment	Unit	Modified Schedule Qty	Qty of Work done	% Of Work done	Start Date	End Date	No. of Working Days
26	Providing and laying in position reinforced cementconcrete of design mix M25 with OPC cement @ 340kgs, with 20mm and down size graded granite metal coarse aggregates @0.70cum andfine aggregtes @ 0.47cum,with superplastisiser @3lts confirming to IS 9103-1999 Reaffirmed-2008, machine mixed,	Sqm	3.57	0	0	20-01-21	08-02-23	749
27	Providing and laying cement concrete using 20 mm and down size granite coarse aggregates and fine aggregates of ready mixed concrete (RMC) for R.C.C works laid in 15 cms thick layers and well compacted including vibrating, curing, etc for all super Structure works with all lead and Lift etc., complete (exclusive of	Cum	259.02	126.87	49	25-10-21	24-11-21	30
28	Providing and laying in position reinforced cement concrete of design mix M20 with OPC cement @ 27.20kgs, with 12mm and down size graded granite metal coarse aggregates @0.5865cum and fine aggregtes @ 0.391cum, with superplastisiser @0.225lts, machine mixed, well compacted for plain chajja of 8.5 cms.	Cum	18.36	36.07	100	14-11-21	24-12-21	40
29	Providing and laying in position reinforced cement concrete of design mix M20 with OPC cement @ 27.20kgs, with 12mm and down size graded granite metal coarse aggregates @0.5865cum and fine aggregtes @ 0.391cum, with superplastisiser @0.225lts, machine mixed, well compacted for plain chajja of 8.5 cms.	Cum	18.36	0	0	20-01-21	15-05-22	480
30	Providing and laying in position reinforced cement concrete of design mix M20 with OPC cement @ 27.20kgs, with 12mm and down size graded granite metal coarse aggregates @0.5865cum and fine aggregtes @ 0.391cum, with superplastisiser @0.225lts, machine mixed, well compacted for plain chajja of 8.5 cms.	tonne	1.08	0	0	20-01-21	08-02-23	749
31	Providing T.M.T bars Fe 500 steel reinforcement for R.C.C work including straightening, cutting, bending, hooking, placing in position, lapping and / or welding wherever required, tying with binding wire and anchoring to the adjoining members wherever necessary complete as per design (laps, hooks and wastage shall	Cum	54.6	58.46	100	04-11-21	09-12-21	35
32	Providing T.M.T bars Fe 500 steel reinforcement for R.C.C work including straightening, cutting, bending, hooking, placing in position, lapping and / or welding wherever required, tying with binding wire and anchoring to the adjoining members wherever necessary complete as per design (laps, hooks and wastage shall	Sqm	20.84	0	0	20-01-21	08-02-23	749
33	Providing T.M.T bars Fe 500 steel reinforcement for R.C.C work including straightening, cutting, bending, hooking, placing in position, lapping and / or welding wherever required, tying with binding wire and anchoring to the adjoining members wherever necessary complete as per design (laps, hooks and wastage shall	Sqm	1.68	0	0	20-01-21	08-02-23	749
34	Providing and constructing load bearing wall with solid concrete blocks of size 400X200X200mm having block density not less than 1800kg/m3 having a minimum average compressive strength 5.00N/mm2 confirming to IS 2185 (part 1) :2005 and constructed with cement mortar 1:4,as per IS 2572:2005 including cost of	Sqm	506.28	470.28	93	10-01-22	10-04-22	90
35	Providing and constructing load bearing wall with solid concrete blocks of size 400X200X200mm having block density not less than 1800kg/m3 having a minimum average compressive strength 5.00N/mm2 confirming to IS 2185 (part 1) :2005 and constructed with cement mortar 1:4,as per IS 2572:2005 including cost of materials, labour charges, scaffolding, curing, hire charges of machinaries etc., Complete as per specifications and the directions	Cum	484.71	0	0	20-01-21	10-06-22	506
36	Providing and constructing load bearing wall with solid concrete blocks of size 400X200X200mm having block density not less than 1800kg/m3 having a minimum average compressive strength 5.00N/mm2 confirming to IS 2185 (part 1) :2005 and constructed with cement mortar 1:4,as per IS 2572:2005 including cost of	M	61.71	0	0	20-01-21	10-06-22	506
37	Providing and constructing non-load bearing wall with solid concrete blocks of size 400X100X200 having a block density not less than 1800kg/m3 having a minimum average compressive strength of 4.00 N/mm2 conforming to I.S : 2185 (Part 1) : 2005 and constructed with CM 1:4, as per IS 2572:2005 including cost	Sqm	201.84	101.38	50	11-03-22	10-05-22	60
38	Providing and constructing non-load bearing wall with solid concrete blocks of size 400X100X200 having a block density not less than 1800kg/m3 having a minimum average compressive strength of 4.00 N/mm2 conforming to I.S : 2185 (Part 1) : 2005	Cum	237.54	0	0	20-01-21	08-02-23	749

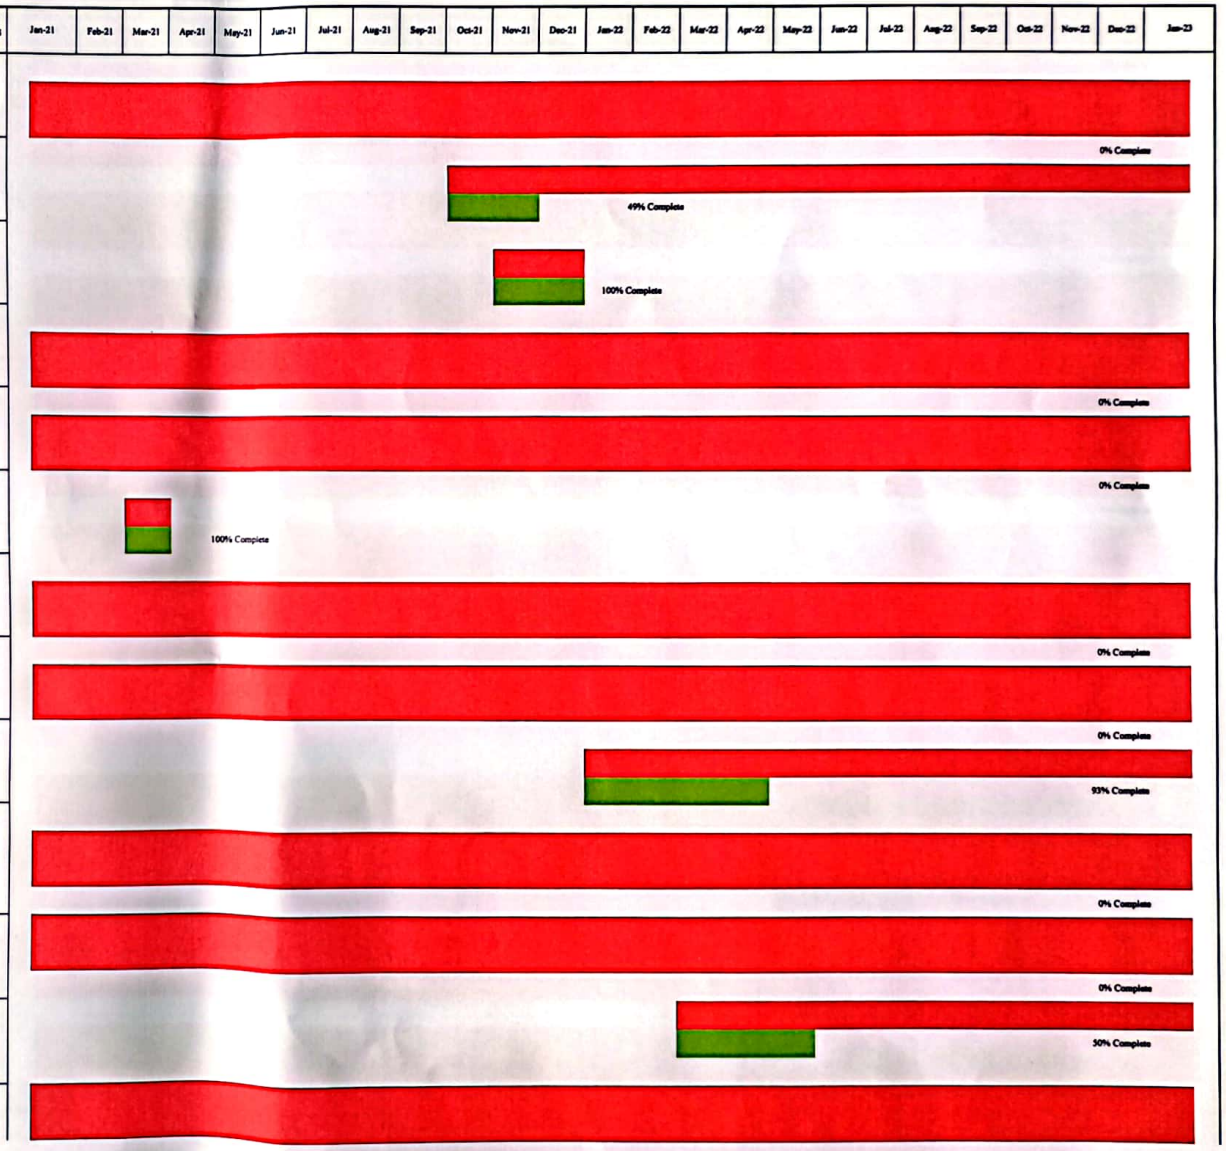

CamScanner

BRUHAT BENGALURU MAHANAGARA PALIKE

Clients Name	:	Executive Engineer Yelahanka Division
Project Name	:	Construction of additional class rooms and compound wall at Govt. Higher primary school (Bangala school) at Yelahanka Old Town in Kempegowda ward no: 01.
Consultants	:	Rudraprasad Consultants
Project Manager /Team Leader	:	Karthik Rechan
Project Start Date	:	20-01-21
Project End Date	:	08-02-23
Project Length in Months	:	25 Months

Sl. No	Assignment	Unit	Modified Schedule Qty	Qty of Work done	% Of Work done	Start Date	End Date	No. of Working Days
	and constructed with CM 1:4, as per IS 2572:2005 including cost							
39	Providing and constructing non-load bearing wall with solid concrete blocks of size 400X100X200 having a block density not less than 1800kg/m3 having a minimum average compressive strength of 4.00 N/mm2 conforming to I.S : 2185 (Part 1) : 2005 and constructed with CM 1:4, as per IS 2572:2005 including cost of all materials, labour charges, scaffolding, curing, hire chargesof machineries etc., Complete as per specifications and the	Each	117.6	0	0	20-01-21	08-02-23	749
40	Providing 18mm thick cement plaster in single coat with cement mortar 1:4, to brick masonry including rounding off corners. wherever required smooth rendering, Providing and removing scaffolding, including cost of materials, labour, curing Complete as per specifications and the directions of the Engineer-in-charge	Each	756.14	0	0	20-01-21	08-02-23	749
41	Providing 18mm thick cement plaster in single coat with cement mortar 1:4, to brick masonry including rounding off corners. wherever required smooth rendering, Providing and removing scaffolding, including cost of materials, labour, curing Complete as per specifications and the directions of the Engineer-in-charge	Cum	807.69	0	0	20-01-21	08-02-23	749
42	Providing 18mm thick cement plaster in single coat with cement mortar 1:4, to brick masonry including rounding off corners. wherever required smooth rendering, Providing and removing scaffolding, including cost of materials, labour, curing Complete as per specifications and the directions of the Engineer-in-charge	Cum	309.9	0	0	20-01-21	08-02-23	749
43	Providing 12mm thick cement plaster in single coat with cement mortar 1:4 , to brick masonry including rounding off corners wherever required smooth rendering, : Providing and removing scaffolding, including cost of materials, labour, curing Complete as per specifications and the directions of the Engineer-in-charge	Cum	744.1	883.21	100	20-01-21	08-02-23	749
44	Providing 12mm thick cement plaster in single coat with cement mortar 1:4 , to brick masonry including rounding off corners wherever required smooth rendering, : Providing and removing scaffolding, including cost of materials, labour, curing Complete as per specifications and the directions of the Engineer-in-charge	Sqm	694.34	0	0	20-01-21	08-02-23	749
45	Providing 12mm thick cement plaster in single coat with cement mortar 1:4 , to brick masonry including rounding off corners wherever required smooth rendering, : Providing and removing scaffolding, including cost of materials, labour, curing Complete as per specifications and the directions of the Engineer-in-charge	Sqm	70.14	0	0	20-01-21	08-02-23	749
46	Providing rough cement plastering 15mm thick in single coat with cement mortar 1:4 to brick masonry for base of dadooing works with sand of approved quality, providing and removing scaffolding, incldng cost of materials, labour, curing Complete as per specifications and the directions of the Engineer-in-charge	Cum	115.71	104.15	90	25-03-22	24-05-22	60
47	Providing rough cement plastering 15mm thick in single coat with cement mortar 1:4 to brick masonry for base of dadooing works with sand of approved quality, providing and removing scaffolding, incldng cost of materials, labour, curing Complete as per specifications and the directions of the Engineer-in-charge	Sqm	111.09	0	0	20-01-21	08-02-23	749
48	Providing 12mm thick cement plaster in single coat with cement mortar 1:4 , to ceiling including rounding off corners wherever required smooth rendering, : including Providing and removing scaffolding, including cost of materials, labour, curingComplete as per specifications and the directions of the Engineer-in-charge Qty	Cum	508.29	528.81	100	04-05-22	23-06-22	50
49	Providing 12mm thick cement plaster in single coat with cement mortar 1:4 , to ceiling including rounding off corners wherever required smooth rendering, : including Providing and removing scaffolding, including cost of materials, labour, curingComplete as per specifications and the directions of the Engineer-in-charge	Sqm	510.24	0	0	20-01-21	08-02-23	749
50	Providing 12mm thick cement plaster in single coat with cement mortar 1:4 , to ceiling including rounding off corners wherever required smooth rendering, : including Providing and removing scaffolding, including cost of materials, labour, curingComplete as per specifications and the directions of the Engineer-in-charge	Sqm	25.90	0.00	0	20-01-21	08-02-23	749

CamScanner

BRUHAT BENGALURU MAHANAGARA PALIKE

Clients Name	:	Executive Engineer Yelahanka Division
Project Name	:	Construction of additional class rooms and compound wall at Govt. Higher primary school (Bangala school) at Yelahanka Old Town in Kempegowda ward no: 01.
Consultants	:	Rudraprasad Consultants
Project Manager /Team Leader	:	Karthik Rechan
Project Start Date	:	20-01-21
Project End Date	:	08-02-23
Project Length in Months	:	25 Months

Sl. No	Assignment	Unit	Modified Schedule Qty	Qty of Work done	% Of Work done	Start Date	End Date	No. of Working Days
51	Providing applying two coats of wall putty to inside plastered walls and ceiling using white cement putty. Scrapping and levelling the surface using steel blade and preparing the surface even and smooth by using different grade sand papers, including cost of all materail cost of labour and scaffolding etc. ,Complete	Sqm	2553.01	5017.02	100	20-12-22	19-01-23	30
52	Providing and applying painting in two coats with plastic emulsion paint of approved brand on wall surface to give an even approved shade after thoroughly brushing the surface, free from mortar drops and other foreign matter including preparing the surface even and sand paper smooth, cost of materials,	Sqm	1508.58	3159.11	100	20-12-22	19-01-23	30
53	Providing and applying two coats with oil bound washable distemper of approved brand and shade on wall surface including priming coat with distemper primer after throughly brooming the surface free from mortar drops and other foreign matter including preparing the surface even and sand paper smooth, cost of	Sqm	1044.43	1866.66	100	30-12-22	13-02-23	45
54	Providing external walls with texture finish using approved brand paint, applied uniformly in three coats over one coat of primer including cost of all materials, machineries, labour, transportation, loading and unloading, all lead and lift and all other incidental charges including scaffolding and removing stains, Complete as	Sqm	774.5	800.06	100	30-12-22	13-02-23	45
55	Providing external walls with texture finish using approved brand paint, applied uniformly in three coats over one coat of primer including cost of all materials, machineries, labour, transportation, loading and unloading, all lead and lift and all other incidental charges including scaffolding and removing stains, Complete as	Sqm	826.05	133.15	100	30-12-22	13-02-23	45
56	Providing external walls with texture finish using approved brand paint, applied uniformly in three coats over one coat of primer including cost of all materials, machineries, labour, transportation, loading and unloading, all lead and lift and all other incidental charges including scaffolding and removing stains, Complete as	Sqm	311.07	114.72	100	30-12-22	13-02-23	45
57	Providing and laying Hassan Green / River Pink granite flooring for staircase, treads and rises using pre polished 20 mm thick water cut green Granite slab laid over existing cement concrete bed in CM 1:3, average 20mm thick including full rounding for nosing , cutting 3 line grooves not more than 2 mm wide for	Sqm	61.02	33.7	55	06-06-22	31-07-22	55
58	Providing and laying Hassan Green / River Pink granite flooring for staircase, treads and rises using pre polished 20 mm thick water cut green Granite slab laid over existing cement concrete bed in CM 1:3, average 20mm thick including full rounding for nosing , cutting 3 line grooves not more than 2 mm wide for	Sqm	61.02	0	0	20-01-21	08-02-23	749
59	Providing and laying M-15 cement concrete flooring, 50 mm thick with metallic concrete hardner topping , under layer of 35mm thick m-15 cement concrete using broken granite metal of 20mm and down size, and top layer 50mm thick of metallic cement hardner consisting of mix 1:2 (1 cement hardner mix : 2 granite	Sqm	508.29	536.19	100	06-06-22	31-07-22	55
60	Providing and laying M-15 cement concrete flooring, 50 mm thick with metallic concrete hardner topping , under layer of 35mm thick m-15 cement concrete using broken granite metal of 20mm and down size, and top layer 50mm thick of metallic cement hardner consisting of mix 1:2 (1 cement hardner mix : 2 granite metal 10mm nominal size) by volume, with which metallic hardening compound of approved quality mix in the ratio of 4:1 (	Sqm	510.24	0	0	20-01-21	08-02-23	749
61	Providing and laying M-15 cement concrete flooring, 50 mm thick with metallic concrete hardner topping , under layer of 35mm thick m-15 cement concrete using broken granite metal of 20mm and down size, and top layer 50mm thick of metallic cement hardner consisting of mix 1:2 (1 cement hardner mix : 2 granite	Sqm	25.9	0	0	20-01-21	08-02-23	749
62	Providing and fixing for flooring 20mm thick gang saw water cut sadarhalli gray granite in CM 1:4 proportion, cut to required shape, pattern with paper joints, finished with cement mortar using white cement and colour pigments to match the colour of slab making through pointing with sealant, groves in joints	Sqm	481.73	1000.16	100	06-06-22	31-07-22	55
63	Providing and fixing for flooring 20mm thick gang saw water cut sadarhalli gray granite in CM 1:4 proportion, cut to required shape, pattern with paper joints, finished with cement mortar using white cement and colour pigments to match the colour of slab making through pointing with sealant, groves in joints	Sqm	483.33	645.98	100	16-06-22	15-08-22	60

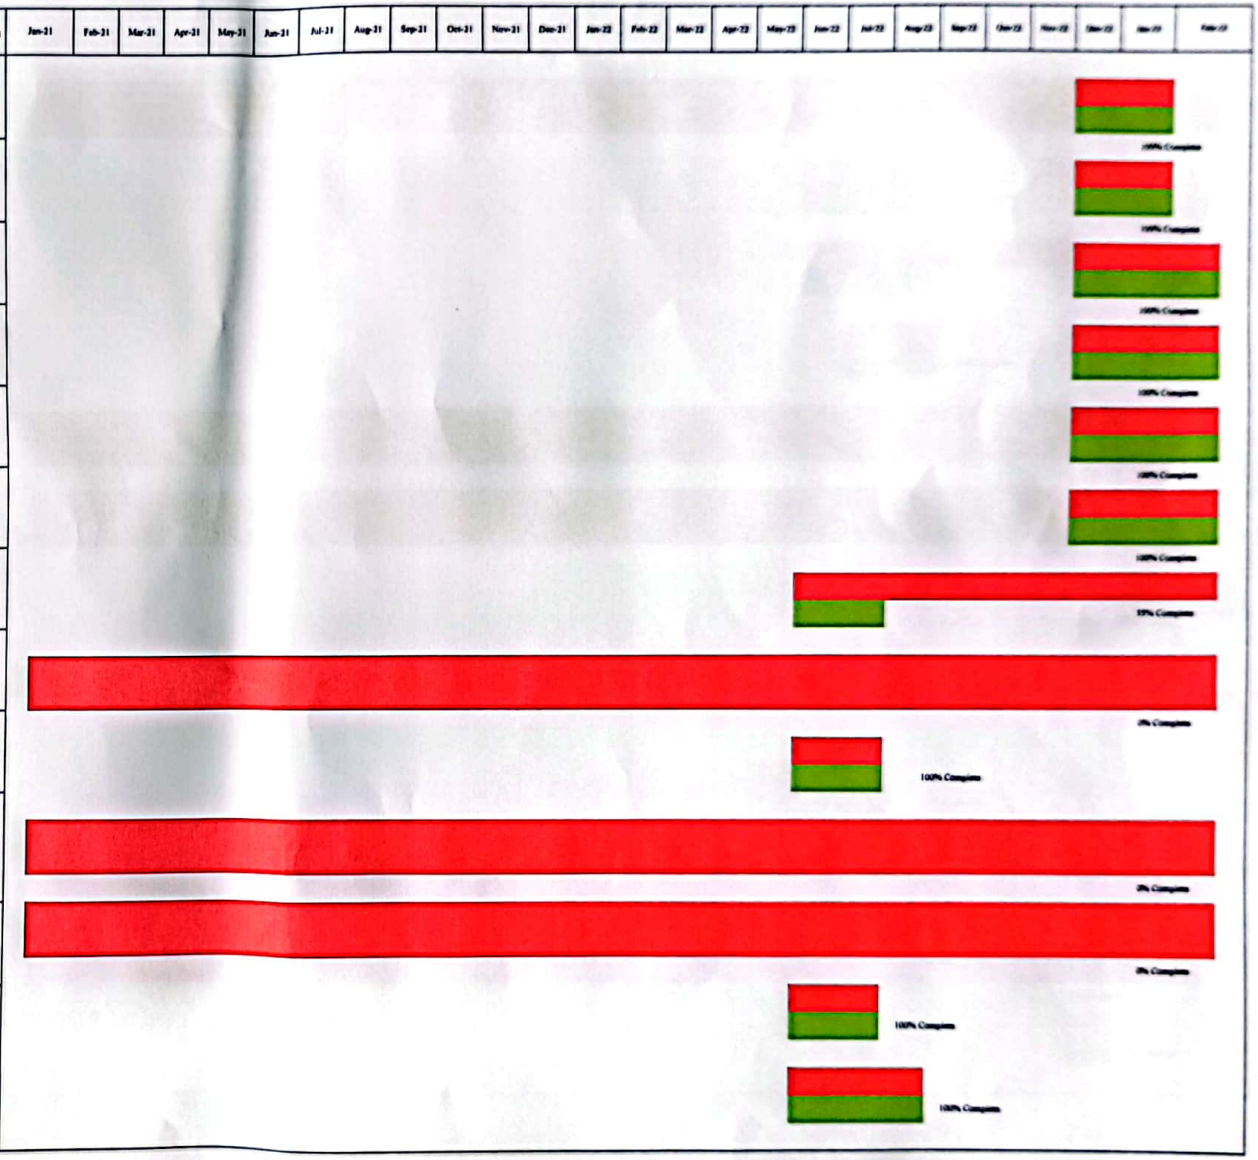

CamScanner

BRUHAT BENGALURU MAHANAGARA PALIKE

Clients Name	:	Executive Engineer Yelahanka Division
Project Name	:	Construction of additional class rooms and compound wall at Govt. Higher primary school (Bangala school) at Yelahanka Old Town in Kempegowda ward no: 01.
Consultants	:	Rudraprasad Consultants
Project Manager /Team Leader	:	Karthik Rechan
Project Start Date	:	20-01-21
Project End Date	:	08-02-23
Project Length in Months	:	25 Months

Sl. No	Assignment	Unit	Modified Schedule Qty	Qty of Work done	% Of Work done	Start Date	End Date	No. of Working Days
64	Providing and fixing for flooring 20mm thick gang saw water cut sadarhalli gray granite in CM 1:4 proportion, cut to required shape, pattern with paper joints, finished with cement mortar using white cement and colour pigments to match the colour of slab making through jointing with sealant, groves in joints including cost of curing - minimum width of 900mmComplete as per specifications and the directions of the Engineer-in-charge	Sqm	25.9	0	0	20-01-21	08-02-23	749
65	Providing skirting, dado, rises of steps with colour glazed tiles 30X60 cms 6mm thick with border of size 30 x 10 cms on 10mm thick cement plaster 1:3 and jointed with white cement slurry over rough plaster surface (excluding cost of rough plastered surface which should be measured and paid separately) using glazed tiles	Sqm	115.71	134.32	100	16-06-22	15-08-22	60
66	Providing skirting, dado, rises of steps with colour glazed tiles 30X60 cms 6mm thick with border of size 30 x 10 cms on 10mm thick cement plaster 1:3 and jointed with white cement slurry over rough plaster surface (excluding cost of rough plastered surface which should be measured and paid separately) using glazed tiles	Sqm	111.09	36.76	33	16-06-22	15-08-22	60
67	Providing Ceramic tiles of size 30x30cms 6mm thick of approved make ,shade and size for flooring, treads of steps and landings laid on a bed of 12mm thick, cement mortar 1:3 mix, flush pointing with white cement using colour pigment , including cost of materials, labour, curing, Complete as per specifications	Sqm	29.76	29.65	100	06-07-22	10-08-22	35
68	Providing Ceramic tiles of size 30x30cms 6mm thick of approved make ,shade and size for flooring, treads of steps and landings laid on a bed of 12mm thick, cement mortar 1:3 mix, flush pointing with white cement using colour pigment , including cost of materials, labour, curing, Complete as per specifications	Sqm	30.1	0	0	20-01-21	08-02-23	749
69	Providing and laying integral cement based waterproofing treatment including preparation of surface as required for treatment of roofs, balconies, terraces etc., consisting of following application. (a) Applying and grouting a slurry coat of neat cement using 2.75 kg/sqm of cement admixed with proprietary	Cum	571.45	0	0	20-01-21	08-02-23	749
70	Fixing of door frames in an existing opening including embedding frame in floor and walls after cutting masonary for holdfasts for embedding boldfast in cement concrete 1:3:6 of 20mm and downsize granite metal painting two coats of coal tar to sides of frame,making good the damages to walls and floor as	Nos	17	24	100	03-01-23	23-01-23	20
71	Providing Honne wood frames of doors, windows, clerestory windows,ventilators and other frames , wrought, framed or assembled including making plaster groves (excluding cost of cement concrete and side clamps),but including cost of materials, labour, HOM of machineries Complete as per specifications and	Cum	1.97	2.81	100	03-01-23	23-01-23	20
72	Providing and fixing in position fully panelled Honne wood shutters for doors, styles and rails of 40mm. thick with bottom and lock rails 180mm wide top rail and styles 100mm wide as per drawing and panels of 25mm thick including cost of materials, labour, HOM of machineries Complete as per specifications and	Sqm	21.42	55.87	100	03-01-23	23-01-23	20
73	Providing and fixing in position fully panelled Honne wood shutters for doors, styles and rails of 40mm. thick with bottom and lock rails 180mm wide top rail and styles 100mm wide as per drawing and panels of 25mm thick including cost of materials, labour, HOM of machineries Complete as per specifications and	Sqm	17.64	0	0	20-01-21	08-02-23	749
74	Providing and fixing in position fully panelled Honne wood shutters for doors, styles and rails of 40mm. thick with bottom and lock rails 180mm wide top rail and styles 100mm wide as per drawing and panels of 25mm thick including cost of materials, labour, HOM of machineries Complete as per specifications and	Sqm	1.89	0	0	20-01-21	08-02-23	749
75	Providing and applying painting two coats (excluding priming coat) on new wood surface and / or wood based surface with enamel paint to give an even shade, cleaning the surface of all dirt, dust and foreign matter, sand papering including cost ofmaterials, labour,Complete as per specifications and the directions of the Engineer-in-charge Qty upto 125%	Sqm	43.34	94.63	100	03-01-23	23-01-23	20

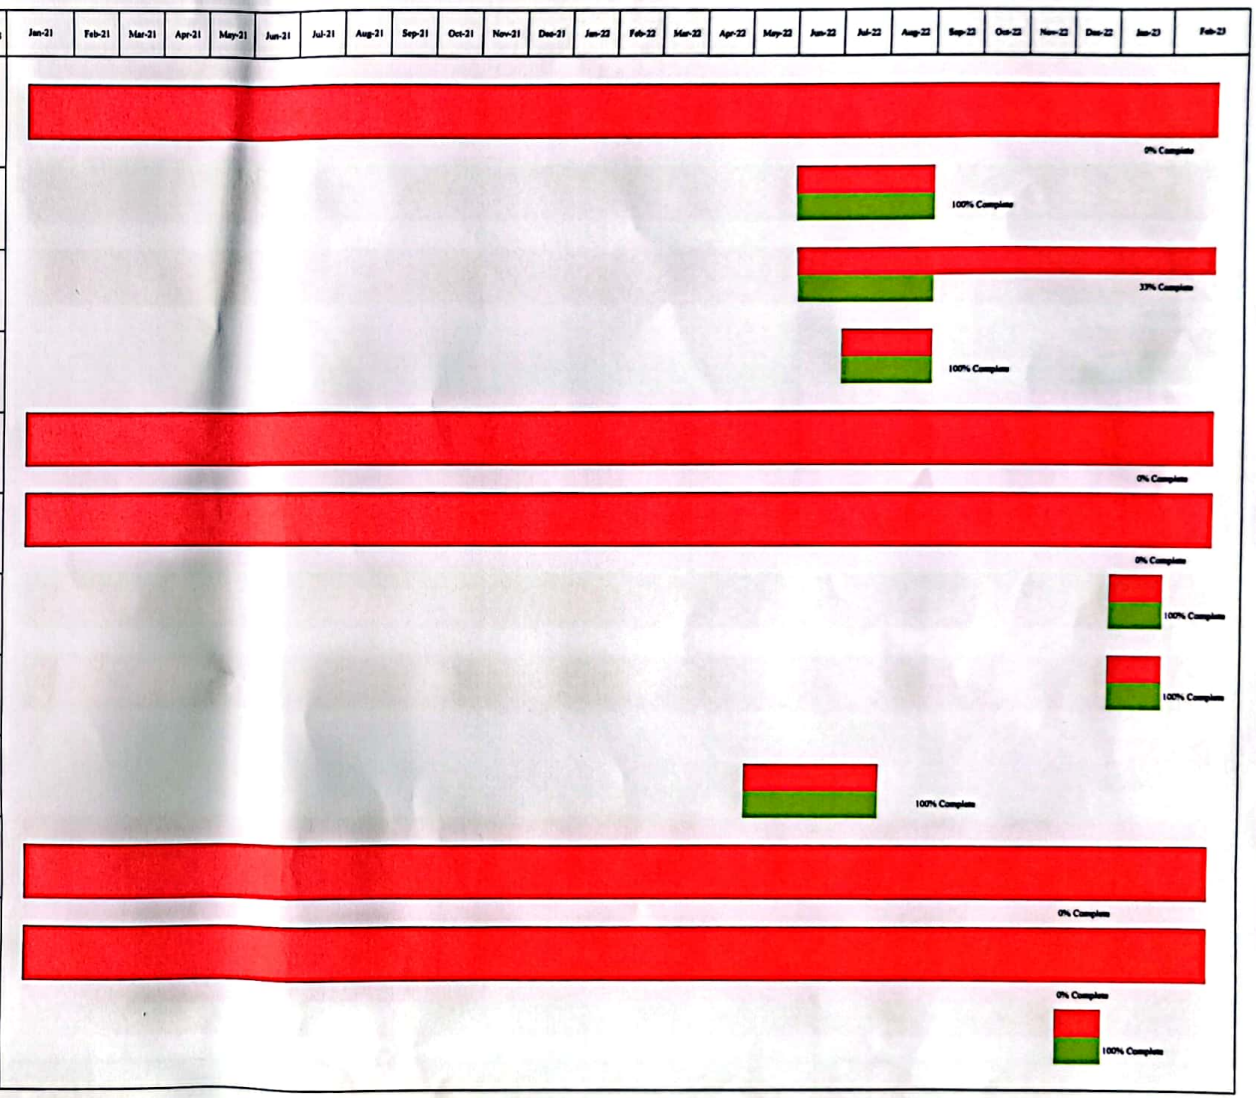

CamScanner

BRUHAT BENGALURU MAHANAGARA PALIKE

Clients Name	:	Executive Engineer Yelahanka Division
Project Name	:	Construction of additional class rooms and compound wall at Govt. Higher primary school (Bangala school) at Yelahanka Old Town in Kempegowda ward no: 01.
Consultants	:	Rudraprasad Consultants
Project Manager /Team Leader	:	Karthik Rechan
Project Start Date	:	20-01-21
Project End Date	:	08-02-23
Project Length in Months	:	25 Months

Sl. No	Assignment	Unit	Modified Schedule Qty	Qty of Work done	% Of Work done	Start Date	End Date	No. of Working Days
76	Providing and fixing 65mmx90mm GRP Doorframe fabricated using E-Glass Chopped Strand Mat (CSM). U.V-stabilized Isopthalic Gelcoat and Isopthalic resin. The thickness of the GRP skin shall not be less than 2.0 mm. The doorframe consists of four segmens, which are provided with plug-in-socket arrangement in-	m	28.5	34.3	100	28-12-22	27-01-23	30
77	Providing and fixing 65mmx90mm GRP Doorframe fabricated using E-Glass Chopped Strand Mat (CSM). U.V-stabilized Isopthalic Gelcoat and Isopthalic resin. The thickness of the GRP skin shall not be less than 2.0 mm. The doorframe consists of four segmens, which are provided with plug-in-socket arrangement in-	m	45.6	0	0	20-01-21	08-02-23	749
78	Providing and fixing 65mmx90mm GRP Doorframe fabricated using E-Glass Chopped Strand Mat (CSM). U.V-stabilized Isopthalic Gelcoat and Isopthalic resin. The thickness of the GRP skin shall not be less than 2.0 mm. The doorframe consists of four segmens, which are provided with plug-in-socket arrangement in-	m	5.7	0	0	20-01-21	08-02-23	749
79	Providing and fixing factory made single leaf rigid GRP Sandwich composite door shutter of 40 mm thick, laminated with two GRP skins with wood grain finish, fabricated using U.V-stabilized Isopthalic Gelcoat and one layer of 450 gns E-Glass Chopped Strand Mat (CSM), impregnated with orthopthalic polyester resin.	Sqm	7.88	9.56	100	28-12-22	27-01-23	30
80	Providing and fixing factory made single leaf rigid GRP Sandwich composite door shutter of 40 mm thick, laminated with two GRP skins with wood grain finish, fabricated using U.V-stabilized Isopthalic Gelcoat and one layer of 450 gns E-Glass Chopped Strand Mat (CSM), impregnated with orthopthalic polyester resin.	Sqm	12.6	0	0	20-01-21	08-02-23	749
81	Providing and fixing in position aluminium windows and ventilators as per approved drawings with sliding shutters using three track window frame of size 92x31.75mm bottom section 1.3mm thick, weight 1.07kg/m; sides and top sections 1.3 mm, thick, weight 0.933 kg/m.shutter frame section comprising top and	Sqm	48.6	0	0	20-01-21	08-02-23	749
82	Providing and fixing in position aluminium windows and ventilators as per approved drawings with sliding shutters using three track window frame of size 92x31.75mm bottom section 1.3mm thick, weight 1.07kg/m; sides and top sections 1.3 mm, thick, weight 0.933 kg/m.shutter frame section comprising top and	Sqm	49.95	0	0	20-01-21	08-02-23	749
83	Providing and fixing in position aluminium windows and ventilators as per approved drawings with sliding shutters using three track window frame of size 92x31.75mm bottom section 1.3mm thick, weight 1.07kg/m; sides and top sections 1.3 mm, thick, weight 0.933 kg/m.shutter frame section comprising top and	Sqm	1.8	0	0	20-01-21	08-02-23	749
84	Providing and fixing M.S grill work for windows and ventilators weighing 21kg/sqm using M.S. flats, or M.S. square rods, or combination of M.S. flats and square rods as per approve design, drawing including cutting steel sections and welding the same to required pattern with a cost of red lead primer, cost of materials,	Kg	1020.6	869.4	85	17-01-23	27-01-23	10
85	Providing and fixing M.S grill work for windows and ventilators weighing 21kg/sqm using M.S. flats, or M.S. square rods, or combination of M.S. flats and square rods as per approve design, drawing including cutting steel sections and welding the same to required pattern with a cost of red lead primer, cost of materials, fixtures, labour and HOM of machinery Complete as per specifications and the directions of the Engineer-in-charge	Kg	1048.95	0	0	20-01-21	08-02-23	749
86	Providing and fixing M.S grill work for windows and ventilators weighing 21kg/sqm using M.S. flats, or M.S. square rods, or combination of M.S. flats and square rods as per approve design, drawing including cutting steel sections and welding the same to required pattern with a cost of red lead primer, cost of materials,	Kg	35.66	0	0	20-01-21	08-02-23	749
87	Providing and fixing M.S.Grill over existing compound wall as per, using 16mm x 16mm M.S.Square rod at 150mm c/c spacing and 6mm x 40mm M.S. flats at horizontal and 6mm x12mm M.S. flat for ornamental design and providing shop edge design at the vertex of every vertical rods, including welding, grinding wherever	Sqm	62.1	0	0	20-01-21	08-02-23	749

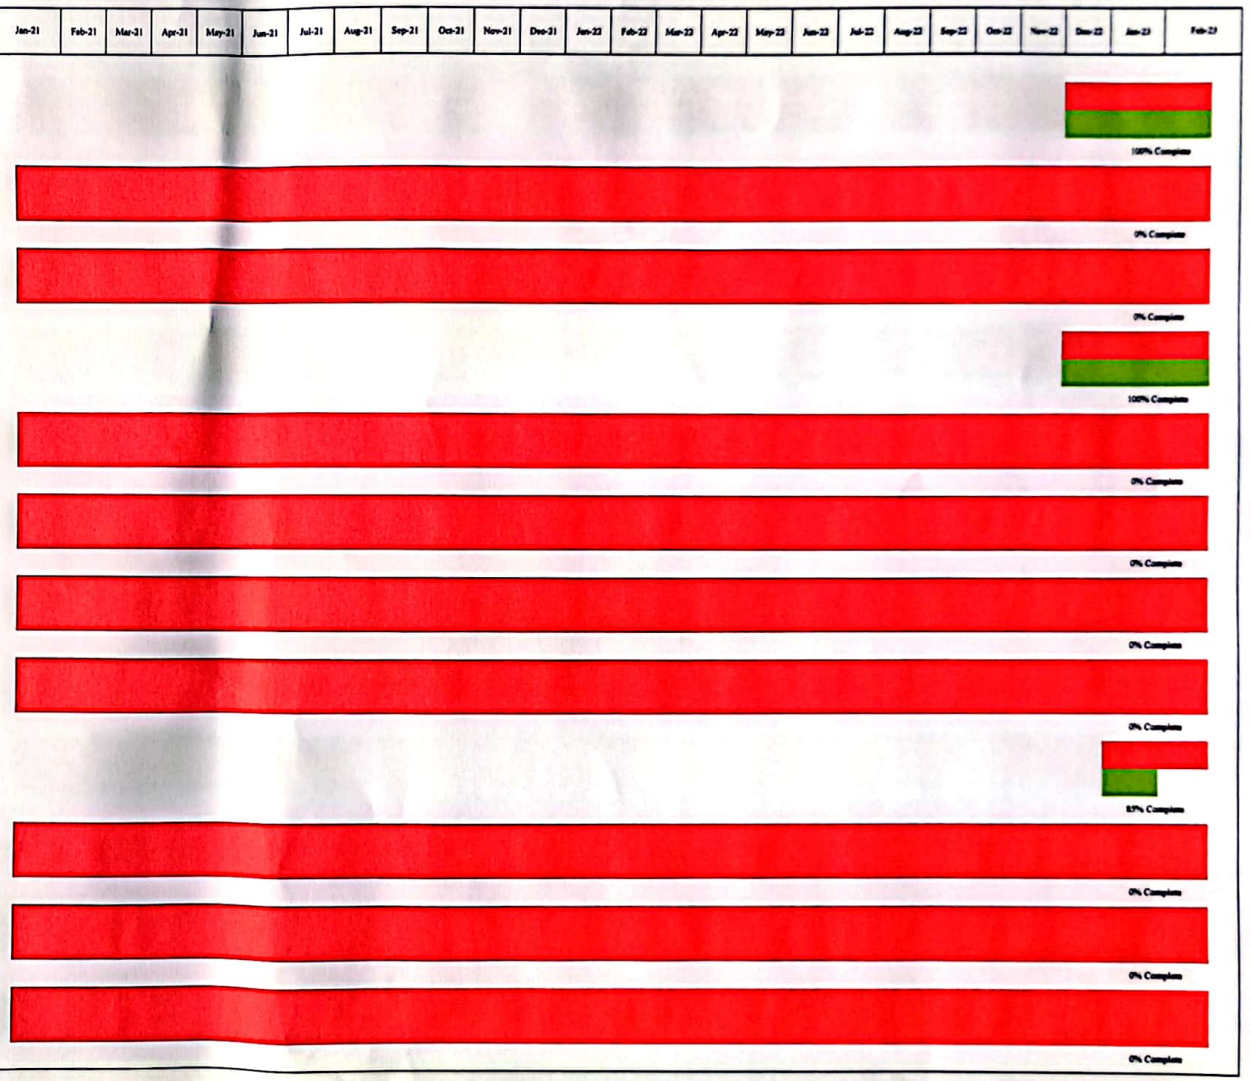

CamScanner

BRUIHAT BENGALURU MAHANAGARA PALIKE

Clients Name	:	Executive Engineer Yelahanka Division
Project Name	:	Construction of additional class rooms and compound wall at Govt. Higher primary school (Bangala school) at Yelahanka Old Town in Kempegowda ward no: 01.
Consultants	:	Rudraprasad Consultants
Project Manager /Team Leader	:	Karthik Rechan
Project Start Date	:	20-01-21
Project End Date	:	08-02-23
Project Length in Months	:	25 Months

Sl. No	Assignment	Unit	Modified Schedule Qty	Qty of Work done	% Of Work done	Start Date	End Date	No of Working Days
88	Providing and fixing M.S.Grill over existing compound wall as per, using 16mm x 16mm M.S.Square rod at 150mm c/c spacing and 6mm x 40mm M.S. flats at horizontal and 6mm x12mm M.S. flat for ornamental design and providing shop edge design at the vertex of every vertical rods, including welding, grinding wherever necessary. All the steel surface should be thoroughly cleaned free of rust and painted with anti corrosive paint (shop paint) etc.,	Sqm	71.3	0	0	20-01-21	08-02-23	749
89	Providing and applying enamel metal paint two coats (excluding priming coat) over new steel or other metal surface brushing to give an even shade after cleaning oil, grease, dirt and other foreign matter, including cost of materials, labour, Complete as per specifications and the directions of the Engineer-in-charge	Sqm	334.1	0	0	20-01-21	08-02-23	749
90	Construction of embankment with approved material Gravel/Murrum with all lifts and leads, transporting to site, spreading, grading to required slope and compacting to meet requirement Table 300- 2 complete as per specifications (Including cost of gravel / murrum, watering	Cum	426.84	0	0	20-01-21	08-02-23	749
91	Providing and fixing Stainless steel staircase raling as per Chief Architect Drawing No. 11520/ HRSC with hand rail 50mm dia 16 guage hollow pipe welded to vertical hollow 50mm dia pipe of 16 guage, stainless steel vertical pipe spaced at 1.20m regular intervals, and 5 Nos of 25mm dia. Stainless steel hollow	Sqm	18.81	0	0	20-01-21	08-02-23	749
92	Providing and fixing Stainless steel staircase raling as per Chief Architect Drawing No. 11520/ HRSC with hand rail 50mm dia 16 guage hollow pipe welded to vertical hollow 50mm dia pipe of 16 guage, stainless steel vertical pipe spaced at 1.20m regular intervals, and 5 Nos of 25mm dia. Stainless steel hollow	Sqm	18.81	0	0	20-01-21	08-02-23	749
93	Providing 20mm square M.S footrest and fixing in manhole Nos 232.00 with M 10 cement concrete block of 20x20x10cms, using 20mm and down size metal of size including cost of materials, labour charges, curingComplete as per specifications and the directions of the Engineer-in-charge	No's	4	0	0	20-01-21	08-02-23	749
94	Waterproofing of RCC Terrace / podium slab / toilet / utilities / water retaining structure by preparing the surface by chipping and cleaning and Grouting of Honey comb, voids,cracks / construction jounts with cement slurry (1kg cement added in 10 ltr of water) added with 100gm of inorganic accelerator, followed by spraying	Sqm	52.94	0	0	20-01-21	08-02-23	749
95	Providing and fixing white vitreous china clay,flat back wash basin size 630x450mm with a pair of 15mm C.P brass pillar taps with C.I / M.S brackets ,32mm C.P brass waste of standard pattern, painting of fittings and brackets, cutting and making good the wall and floor wherever required , including cost of materials,	Unit	6	0	0	20-01-21	08-02-23	749
96	Providing and fixing white vitreous china clay, water closet europeon type (pedestal type, p-trap) with black solid plastic seat and lid, C.P brass hinges, rubber buffers. 10 litre low level,P.V.C flushing cistern (all are approved make) with fittings, C.I / M.S brackets , 40mm diameter flush pipe fittings and clamps, overflow	Each	13	0	0	20-01-21	08-02-23	749
97	Providing and fixing white vitreous china clay,flat back or half stall urinal basin of size 580x380x350mm in the range of two with 7.5 litres P.V.C automatic flushing cistern, C.I / M.S brackets ,standard flush pipe and C.P brass spreaders with brass unions and G.I clamps, C.I trap with outlet grating and other	Unit	4	0	0	20-01-21	08-02-23	749
98	Providing and fixing 453x357mm dia rectangular shape mirror with plastic moulded frame of approved make and shade with 6mm thick hard board backing including cost of materials, labour Complete as per specifications and the directions of the Engineer-in-charge	Unit	6	0	0	20-01-21	08-02-23	749
99	Providing and fixing C.P brass towel rail 740mm length, 20mm dia with C.P brackets, fixed to wooden cleats with C.P brass screws including cost of materials, labourComplete as per specifications and the directions of the Engineer-in-charge	Unit	12	0	0	20-01-21	08-02-23	749
100	Providing and fixing 7.5 cms to 15.00 cms dia NP grating 100 mm dia. Complete as per specifications and the directions of the Engineer-in-charge	Each	30.00	0.00	0	20-01-21	08-02-23	749

CamScanner

BRUHAT BENGALURU MAHANAGARA PALIKE

Clients Name	:	Executive Engineer Yelahanka Division
Project Name	:	Construction of additional class rooms and compound wall at Govt. Higher primary school (Bangala school) at Yelahanka Old Town in Kempegowda ward no: 01.
Consultants	:	Rudraprasad Consultants
Project Manager /Team Leader	:	Karthik Rechan
Project Start Date	:	20-01-21
Project End Date	:	08-02-23
Project Length in Months	:	25 Months

Sl. No	Assignment	Unit	Modified Schedule Qty	Qty of Work done	% Of Work done	Start Date	End Date	No. of Working Days
101	Providing and fixing to wall, ceiling and floor unplasticised PVC 6.00 kgs/sqcm working pressure with pipe fittings, wall clips etc., and making good the wall, ceiling and floor for sanitary pipelines including cost of all materials,labour charges, HOM of acquirements and testing complete as per specifications.For Rain	m	90	0	0	20-01-21	08-02-23	749
102	Providing and fixing to wall, ceiling and floor unplasticised PVC 6.00 kgs/sqcm working pressure with pipe fittings, wall clips etc., and making good the wall, ceiling and floor for sanitary pipelines including cost of all materials,labour charges, HOM of acquirements and testing complete as per specifications.For Rain	m	100	0	0	20-01-21	08-02-23	749
103	Constructing brick masonry inspection chamber 600x600mm, and 450mm depth, (clear inside dimension) for single pipeline, using table moulded non-modular bricks of class designation 50 in cement mortar 1:5, C.I cover withframe (light duty) 455x610mm internal dimensions, total weight of cover with frame to be not less	Nos	8	0	0	20-01-21	08-02-23	749
104	Providing and placing on terrace, polyethylene water storage tanks with manhole lid and suitable locking arrangements, making holes of suitable diameter for inlet, outlet and over flow pipes, including cost of all materials, labour, transport charges, HOM of equipments and testing Complete as per specifications and the	Each	2	0	0	20-01-21	08-02-23	749
105	Providing and fixing in position brass bib cock of approved quality 20mm nominal bore including cost of all materials, labour and HOM of equipments with all leads Complete as per specifications and the directions of the Engineer-in-charge	Each	25	0	0	20-01-21	08-02-23	749
106	Providing and fixing in position brass stop cock of approved quality 20mm nominal bore including cost of all materials, labour and HOM of equipments with all leadsComplete as per specifications and the directions of the Engineer-in-charge	Each	20	0	0	20-01-21	08-02-23	749
107	Providing and fixing in position brass gate valve with C.I wheel of approved quality (screwed end) 20mm nominal bore including cost of all materials, labour and HOM of equipments with all leads Complete as per specifications and the directions of the Engineer-in-charge	Each	4	0	0	20-01-21	08-02-23	749
108	Providing and fixing Chorinated Poly Venyl Chloride (CPVC) pipes conforming to IS 15778, having thermal stability for hot and cold water supply including all CPVC plain and brass threaded fittings including fixing the pipe with clamp at 1.00 mtr spacing. This includes jointing of pipes and fittings with one step CPVC	m	80	0	0	05-10-21	10-06-22	248
109	Providing and fixing Chorinated Poly Venyl Chloride (CPVC) pipes conforming to IS 15778, having thermal stability for hot and cold water supply including all CPVC plain and brass threaded fittings including fixing the pipe with clamp at 1.00 mtr spacing. This includes jointing of pipes and fittings with one step CPVC	m	90	0	0	20-01-21	08-02-23	749
110	Point wiring using copper wire without switch (Class A material). Supplying and wiring adopting loop system in existing PVC conduit/casing capping using 2X1.5Sqmm(phase &Netural) &1X1.0 Sqmm (Earth Wire) FRLSmultistrand PVC insulated 2x1.5sqmm copper confirming to the GTP With a 6Amps flusg type SP control switch shall be fixed on the existing plastic sheet / gand box .the other end of the wire shall be terminated with	Point	250	0	0	20-01-21	08-02-23	749
111	Point wiring using copper wire without switch (Class A material). Supplying and wiring adopting loop system in existing PVC conduit/casing capping using 2X1.5Sqmm(phase &Netural) &1X1.0 Sqmm (Earth Wire) FRLSmultistrand PVC insulated 2x1.5sqmm copper confirming to the GTP With a 6Amps flusg	Point	175	0	0	20-01-21	08-02-23	749
112	Concealed Conduit System - Supplying heavy gague PVC conduit pipe 20/25/32 mm dia 2mm thick confirming to IS 2509 with suitable size bends metal/pvc junction boxes, adhesive paste etc, and running before concreting and slab. The conduit should be tied to the reinforcement rods by using binding wires and	Rm	800	1200	100	26-12-21	10-01-22	15
113	Concealed Conduit System - Supplying heavy gague PVC conduit pipe 20/25/32 mm dia 2mm thick confirming to IS 2509 with suitable size bends metal/pvc junction boxes, adhesive paste etc, and running before concreting and slab. The conduit should be tied to the reinforcement rods by using binding wires and	Rm	1400	2300	100	26-12-21	10-01-22	15

CamScanner

BRUIIAT BENGALURU MAIIANAGARA PALIKE

Clients Name	:	Executive Engineer Yelahanka Division
Project Name	:	Construction of additional class rooms and compound wall at Govt. Higher primary school (Bangala school) at Yelahanka Old Town in Kempegowda ward no: 01.
Consultants	:	Rudraprasad Consultants
Project Manager /Team Leader	:	Karthik Rechan
Project Start Date	:	20-01-21
Project End Date	:	08-02-23
Project Length in Months	:	25 Months

Sl No	Assignment	Unit	Modified Schedule Qty	Qty of Work done	% Of Work done	Start Date	End Date	No. of Working Days
114	Concealed Conduit System - Supplying heavy gague PVC conduit pipe 20/25/32 mm dia 2mm thick confirming to IS 2509 with suitable size bends metal/pvc junction boxes, adhesive paste etc, and running before concreting and slab. The conduit should be tied to the reinforcement rods by using binding wires and unused ways of junction boxes and pipe ends should be covered using PVC end enclosures, run with 18SWG GI fisg wire	Rm	300	500	100	26-12-21	10-01-22	15
115	Groove cutting : Supplying heavy gauge conduit PVC 25/2mm of s thick heavy with suitable size bend , metal junction boxes, adhesive pastes etc, by groove cutting in a wall and fixing by bracing U or J hooks and cement plastering up to the surface and run with 18SWG GI fish wire run throughout the conduit where	Mtr	250	0	0	20-01-21	08-02-23	749
116	Groove cutting : Supplying heavy gauge conduit PVC 25/2mm of s thick heavy with suitable size bend , metal junction boxes, adhesive pastes etc, by groove cutting in a wall and fixing by bracing U or J hooks and cement plastering up to the surface and run with 18SWG GI fish wire run throughout the conduit where	Mtr	800	0	0	20-01-21	30-05-22	495
117	Groove cutting : Supplying heavy gauge conduit PVC 25/2mm of s thick heavy with suitable size bend , metal junction boxes, adhesive pastes etc, by groove cutting in a wall and fixing by bracing U or J hooks and cement plastering up to the surface and run with 18SWG GI fish wire run throughout the conduit where	Mtr	450	0	0	30-10-21	30-05-22	212
118	Supplying and flush modular poweder coated / galvanized metal box suitable for mounting modular switch plates. the box should be firmil flush mounted after due groove cutting in brick /stone/C.C wall 1 - 3 Way Complete as per specifications and the directions of the Engineer-in-charge	Each	200	0	0	25-10-21	21-06-22	239
119	Supplying and flush modular poweder coated / galvanized metal box suitable for mounting modular switch plates. the box should be firmil flush mounted after due groove cutting in brick /stone/C.C wall 4 - 5 Way Complete as per specifications and the directions of the Engineer-in-charge	Each	175	0	0	25-10-21	21-06-22	239
120	Supplying 6A flush type socket and 6 amp flush type SP switch either surface/flush mountinh in existing gang box or in 4mm thik plastic sheet and fixing over a flush mounted wooden box and wiring using necessary capacity wire as required as per IS 1293 and IS 3654 . 6AMP 3/5 and Switch Complete as per	Each	250	0	0	25-10-21	21-06-22	239
121	Supplying and mounting 2 Nos, of 2 Way 6amps flush type switches either surface/flush mounted on existing gang box or in 4mm thick plastic sheet and mounted on a flusg mounted wooden box and wiring as per IS 1293 Complete as per specifications and the directions of the Engineer-in-charge	Each	100	0	0	25-10-21	21-06-22	239
122	Supply and fixing of bakelite D.P /socket/switch with/ without neon indicator over existing wood board or flush mounting in plastic plates/nitches as per IS 1293 and IS 3854 16Amps Combined switch and socket with indication Complete as per specifications and the directions of the Engineer-in-charge	No's	75	0	0	25-10-21	21-06-22	239
123	Electronic stepped regulator. Complete as per specifications and the directions of the Engineer-in-charge	No's	166	0	0	25-10-21	21-06-22	239
124	Wiring for lighting/power circuit using Grade using one of FRLS PVC insulated 1100 volts grade, multistrand copper with low conductor resistance single core wire in open or concealed system of wiring. With specified IS-694: confirming to Latest amendements. 1.5sqmm Complete as per specifications and the	Rm	625	0	0	25-10-21	21-06-22	239
125	Wiring for lighting/power circuit using Grade using one of FRLS PVC insulated 1100 volts grade, multistrand copper with low conductor resistance single core wire in open or concealed system of wiring. With specified IS-694: confirming to Latest amendements. 2.5sqmm Complete as per specifications and the	Rm	1600.00	0.00	0	25-10-21	21-06-22	239

Dewa.

CamScanner

BRUHAT BENGALURU MAHANAGARA PALIKE

Clients Name	:	Executive Engineer Yelahanka Division
Project Name	:	Construction of additional class rooms and compound wall at Govt. Higher primary school (Bangala school) at Yelahanka Old Town in Kempegowda ward no: 01.
Consultants	:	Rudraprasad Consultants
Project Manager /Team Leader	:	Karthik Rechan
Project Start Date	:	20-01-21
Project End Date	:	08-02-23
Project Length in Months	:	25 Months

Sl. No	Assignment	Unit	Modified Schedule Qty	Qty of Work done	% Of Work done	Start Date	End Date	No. of Working Days
126	Wiring for lighting/power circuit using Grade using one of FRLS PVC insulated 1100 volts grade, multistrand copper with low conductor resistance single core wire in open or concealed system of wiring. With specified IS-694: confirming to Latest amendements. 4sqmm Complete as per specifications and the	Rm	950	0	0	20-01-21	08-02-23	749
127	Supplying and fixing Metal Fan Box with Round Hook Complete as per specifications and the directions of the Engineer-in-charge	Nos	166	0	0	20-01-21	08-02-23	749
128	Supplying and fixing of Group A, regular MCB distribution boards on wall/woodboard/flush mounting using required clamps, bolts, nuts etc., with provision for fixing suitable type capacity MCB'S single phase/ 3 phase / single door with powder coated painting made out of SWG MS enclosute 12 way SP & N	Nos	30	0	0	20-01-21	08-02-23	749
129	Supply and fixing miniature circuit breakers on the existing MCB distribution boards using necessary fixing meterials and "C" type curve, Indiator ON/OFF energy cross -3 with as required confirming to IEC 60898 5-32 AMPS DP Complete as per specifications and the directions of the Engineer-in-charge	Nos	15	0	0	20-01-21	08-02-23	749
130	Supplying, fixing and wiring earth electrode for grounding conduits , I.C. cutouts and others equipments on the meter board using 40mm dia 2.90mm long buried in a pit.. the pit should be filled with equal proportion of salt and charcoal 150mm all-round the pipe to complete depth. The connection from the pipe to the	Nos	2	0	0	20-01-21	08-02-23	749
131	Supplying and running of GI/ copper strips for grounding connections, using necessary fixing materials as required. 25 x 3mm G.I strip Complete as per specifications and the directions of the Engineer-in-charge	Mtr	80	0	0	20-01-21	08-02-23	749
132	Supplying of ___feet - PVC Batten with integrated LED tube ___W with high quality diffuser with Life of 25000 burning hours & 70% lumen maintenance with CRI > 80. Power Input: 220-240V @ 50/60Hz & Power factor >0.9 along with CE approved. 2 years Warranty against any manufacturing defect working under	Each	350	0	0	20-01-21	08-02-23	749
133	Supplying & fixing retrofit type -PL- LED Lamp .....W LED linear source with CCT 6500 degree K, CRI> 70%. efficacy >80 lumen per watt, life> 25000 burning hours and Compliance to IS 10322/IEC 60598, LM 79 & LM 80. The LED are driven by HF electronic driver integrated	Each	100	0	0	20-01-21	08-02-23	749
134	Supplying capacitor type ceiling fan complete with down rod blades shackle, canopies etc, for operation on 230 volts, 50 cycles. single phase AC supply conforming to ISS-374-1979 and with double ball bearing system 48" sweep (1200mm) Complete as per specifications and the directions of the Engineer-in-charge	Each	166	0	0	20-01-21	08-02-23	749
135	Supply Exhaust fan if 1440 RPM of (12") size with dracket blades complete for light duty suitable to -oerate on 230V 50Hz, supply Complete as per specifications and the directions of the Engineer-in-charge	Each	35	0	0	20-01-21	08-02-23	749
136	Supplying and fixing Trivector meter suitable for operation LT operation and CT operated meter in polycarbonate body in class 0.5accuracy as per IS 14697 and completely wired Complete as per specifications and the directions of the Engineer-in-charge	Each	2	0	0	20-01-21	08-02-23	749
137	Supplying and fixing of LED type panel board indicating lamp with required colour suitable for 220v A.C. 50 Hz 12/24v D.C (48/6.36) Complete as per specifications and the directions of the Engineer-in-charge	Each	2	0	0	20-01-21	08-02-23	749

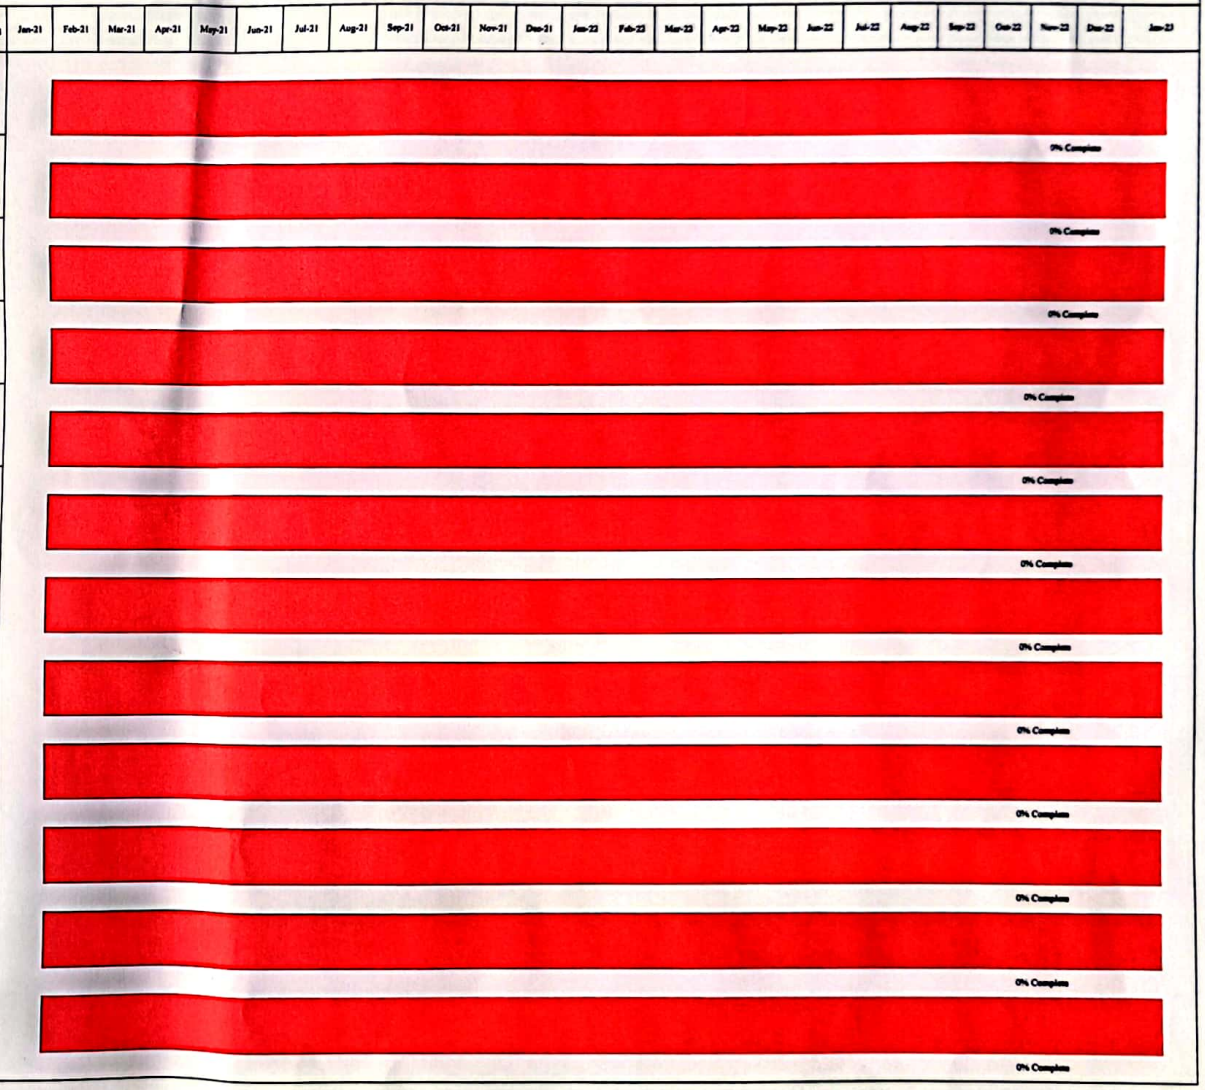

BRUHAT BENGALURU MAHANAGARA PALIKE

Clients Name	:	Executive Engineer Yelahanka Division
Project Name	:	Construction of additional class rooms and compound wall at Govt. Higher primary school (Bangala school) at Yelahanka Old Town in Kempegowda ward no: 01.
Consultants	:	Rudraprasad Consultants
Project Manager /Team Leader	:	Karthik Rechan
Project Start Date	:	20-01-21
Project End Date	:	08-02-23
Project Length in Months	:	25 Months

Sl. No	Assignment	Unit	Modified Schedule Qty	Qty of Work done	% Of Work done	Start Date	End Date	No. of Working Days	Jan-21	Feb-21	Mar-21	Apr-21	May-21	Jun-21	Jul-21	Aug-21	Sep-21	Oct-21	Nov-21	Dec-21	Jan-22	Feb-22	Mar-22	Apr-22	May-22	Jun-22	Jul-22	Aug-22	Sep-22	Oct-22	Nov-22	Dec-22	Jan-23
149	Supplying and fixing of class A (medium duty) GI pipe of wall thick ness not less than 3.25mm on pole/wall/drain crossing with necessary clamping arrangements for UG cable of 1.1 KV class. (68/7.12) 65mm Complete as per specifications and the directions of the Engineer-in-charge	Mtr	30	0	0	20-01-21	08-02-23	749																									

= Planned %

= Executed %

Asst. Executive Engineer
Yelahanka Sub. Divison
(BBMP Ynk. Zn)
Yelahanka, Bangalore

RUDRAPRASAD CONSULTANTS
BANGALORE
